
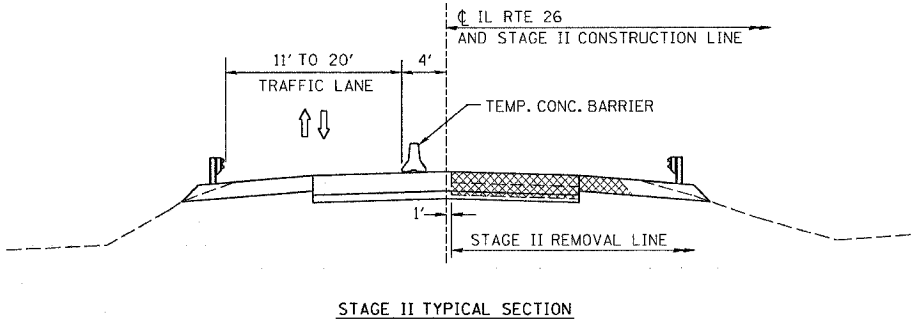


SEQUENCE OF OPERATIONS						
PHASE	A			B		
INTERVAL	1	2	3	4	5	6
NORTHBOUND OR EASTBOUND	G	Y	R	R	R	R
SOUTHBOUND OR WESTBOUND	R	R	R	G	Y	R

MAINTENANCE OF TRAFFIC  
STAGE II

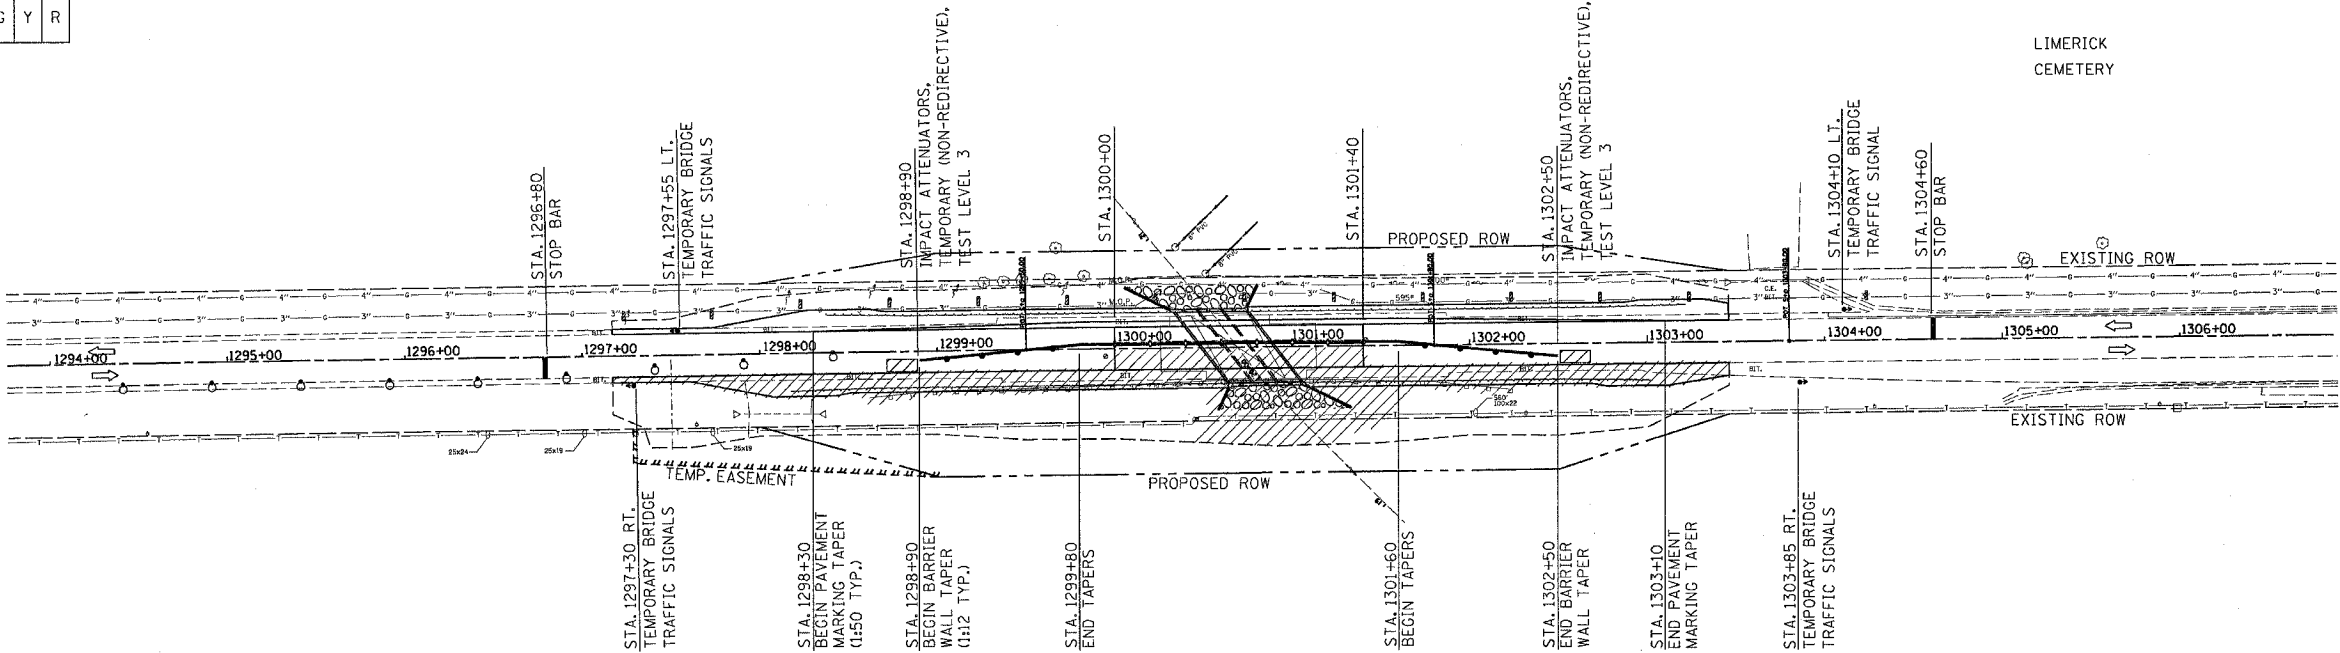

LEGEND


- Work area
- Removal Area
- Drum with steady burning light
- Traffic signal
- Double vertical panel
- Type C Bidirectional reflector
- Sand module impact attenuator
- Steady burning lights and double vertical panels

STAGE II CONSTRUCTION

- CLOSE WEST 1/2 OF IL 26 IN ACCORDANCE WITH HWY. STD. 701321.
- REMOVE WEST 1/2 OF EXISTING BRIDGE, PAVEMENT, SHOULDERS, AND WEST SIDE OF GUARDRAIL AS SCHEDULED.
- CONSTRUCT WEST 1/2 OF PROPOSED BOX CULVERT AND PAVEMENT PATCHING, PLACE DOWNSTREAM RIPRAP AND GRADE DOWNSTREAM CHANNEL. CONSTRUCT PROPOSED SHOULDER BASE COURSE AND GUARDRAIL.

GENERAL NOTES:

- MAINTENANCE OF TRAFFIC SHALL BE IN ACCORDANCE WITH HWY. STD. 701321 AS SPECIFIED, AND AS DIRECTED BY THE ENGINEER.
- THE SIGN "TO ACTUATE SIGNAL" SHOWN IN DISTRICT STANDARD 99.4 SHALL BE INSTALLED AT THE STOP LINE AS DIRECTED BY ENGINEER.
- SIGNALS, STOP BARS AND ADVANCE WARNING SIGNS SHALL REMAIN AT THE SAME LOCATIONS FOR THE DURATION OF STAGE I & II.



REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION  
  
MAINTENANCE OF TRAFFIC

SCALE: 1" = 50'  
DATE 04/04

DRAWN BY WX  
CHECKED BY IYL
