


F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
22	16R	WHITESIDE	201	60
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	
CONTRACT NO. 64656				

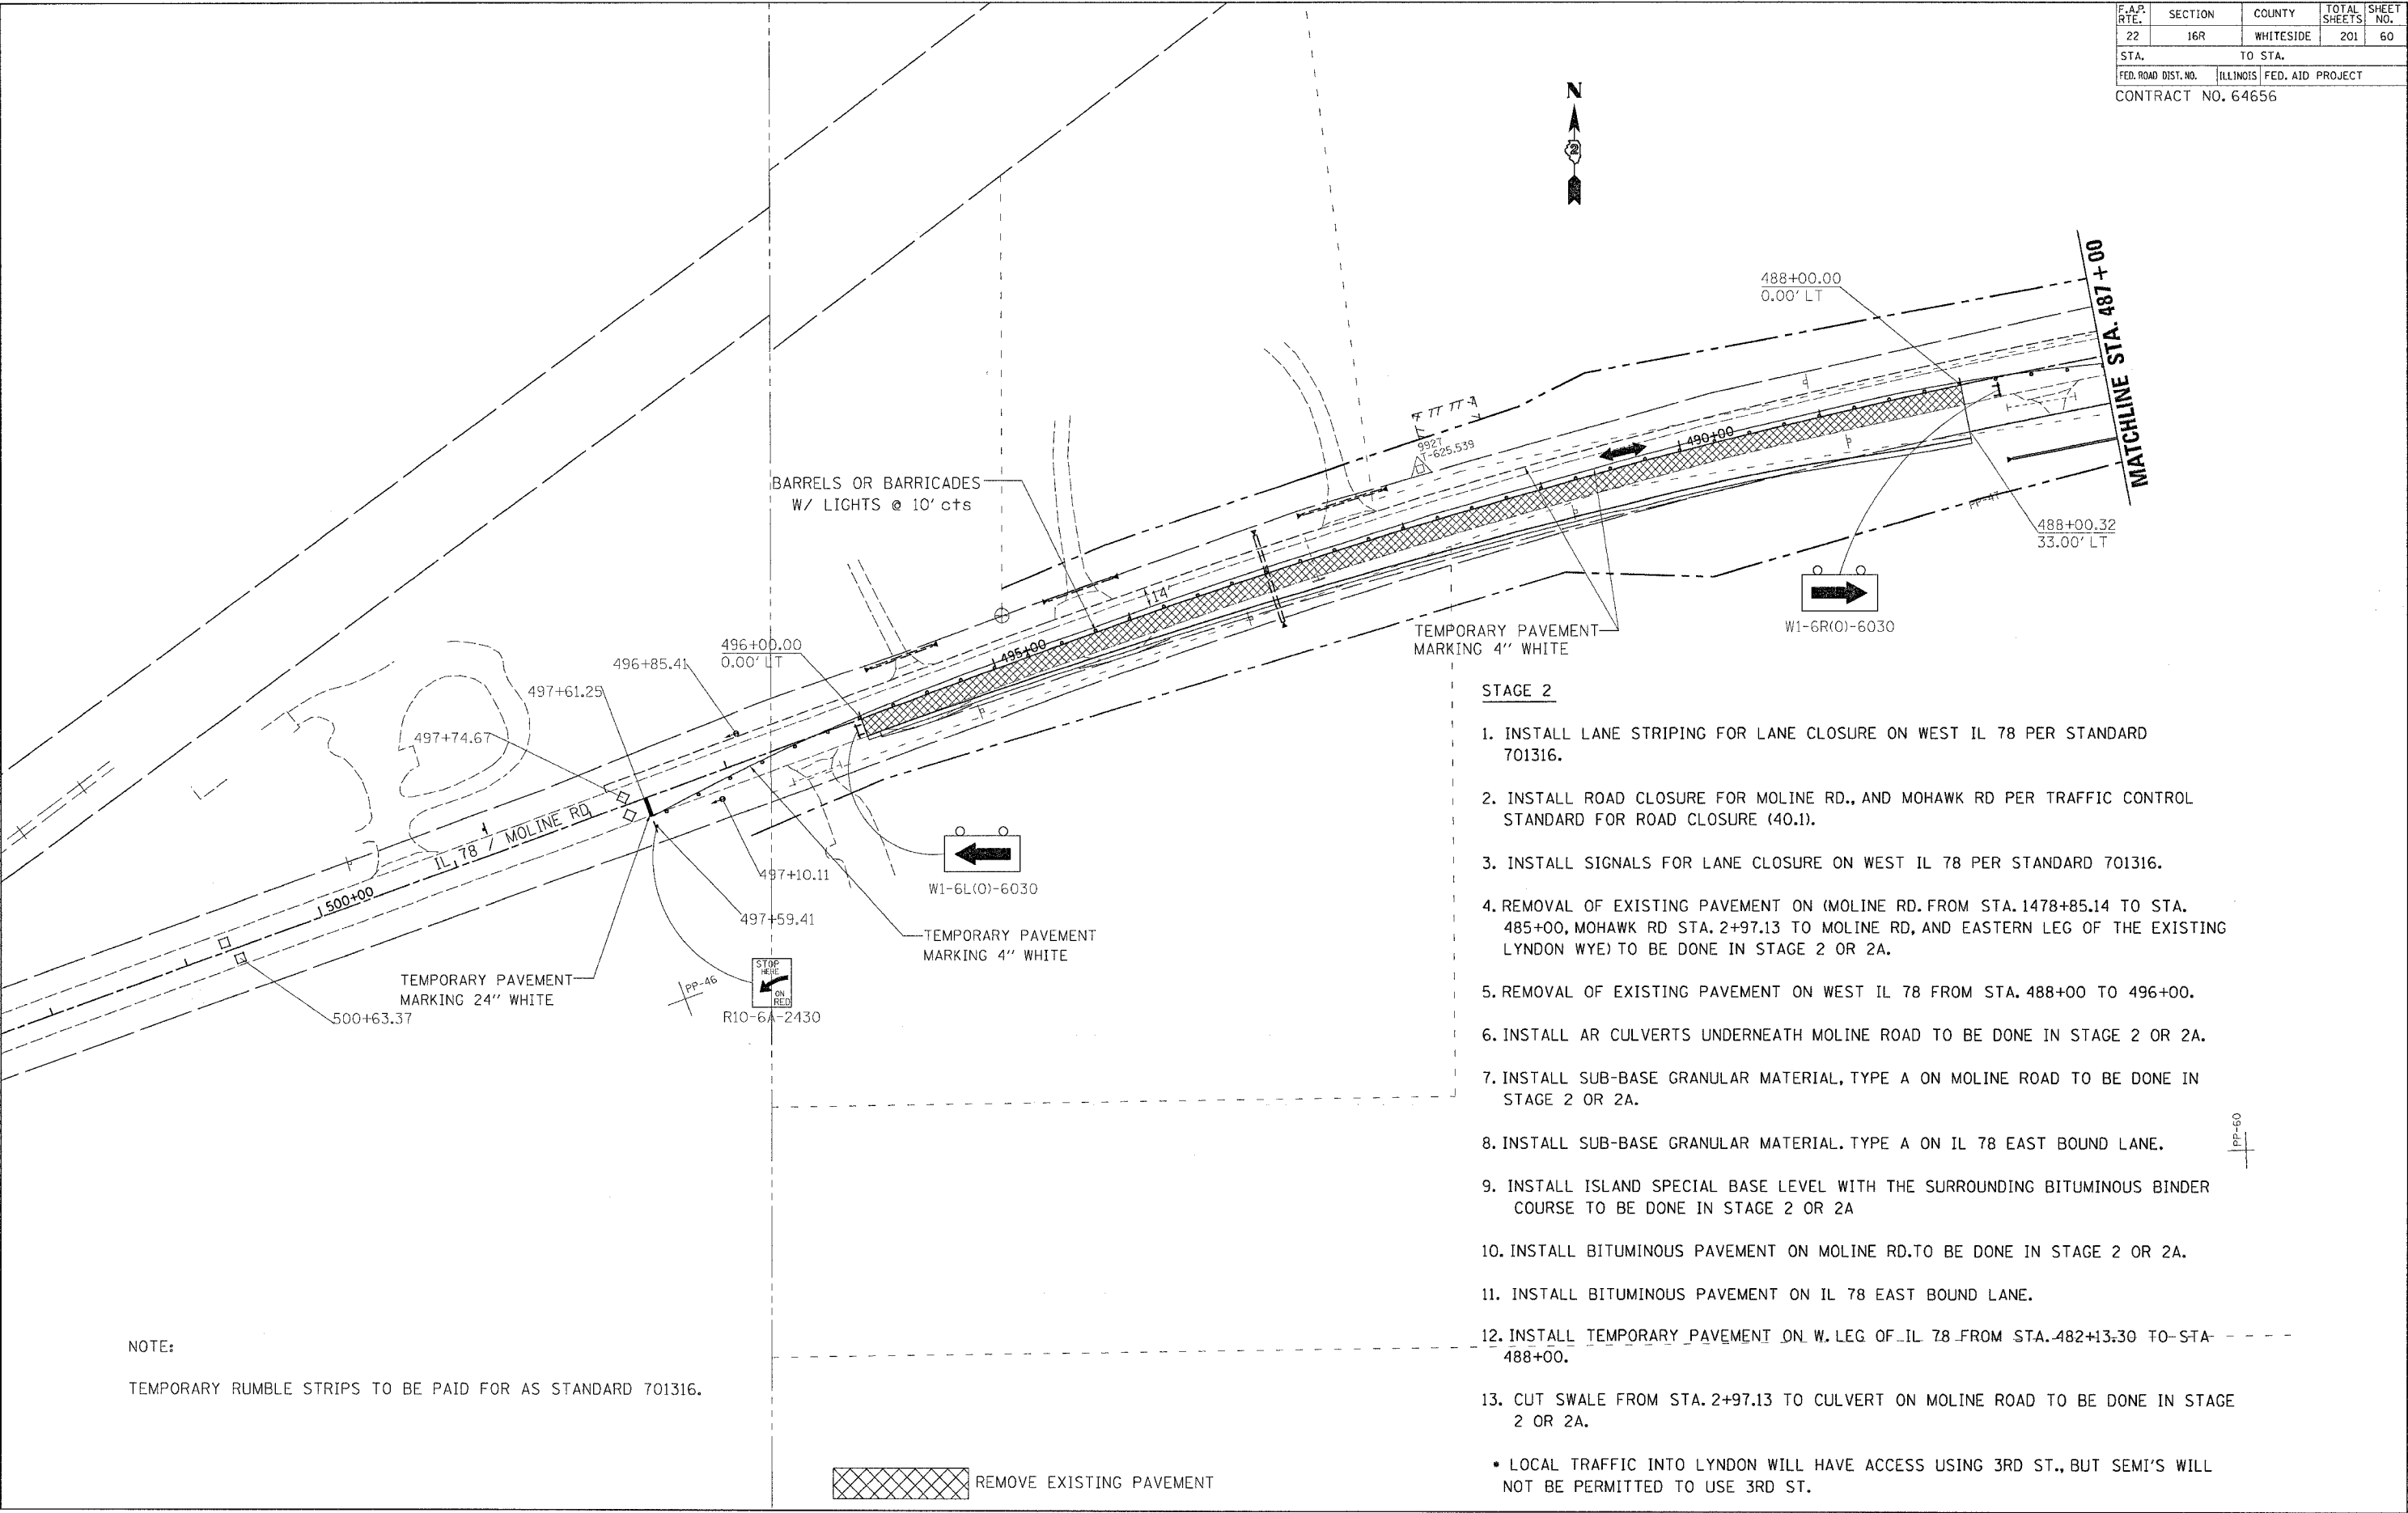

NOTE:  
TEMPORARY RUMBLE STRIPS TO BE PAID FOR AS STANDARD 701316.

- STAGE 2**
1. INSTALL LANE STRIPING FOR LANE CLOSURE ON WEST IL 78 PER STANDARD 701316.
  2. INSTALL ROAD CLOSURE FOR MOLINE RD., AND MOHAWK RD PER TRAFFIC CONTROL STANDARD FOR ROAD CLOSURE (40.1).
  3. INSTALL SIGNALS FOR LANE CLOSURE ON WEST IL 78 PER STANDARD 701316.
  4. REMOVAL OF EXISTING PAVEMENT ON (MOLINE RD. FROM STA. 1478+85.14 TO STA. 485+00, MOHAWK RD STA. 2+97.13 TO MOLINE RD, AND EASTERN LEG OF THE EXISTING LYNDON WYE) TO BE DONE IN STAGE 2 OR 2A.
  5. REMOVAL OF EXISTING PAVEMENT ON WEST IL 78 FROM STA. 488+00 TO 496+00.
  6. INSTALL AR CULVERTS UNDERNEATH MOLINE ROAD TO BE DONE IN STAGE 2 OR 2A.
  7. INSTALL SUB-BASE GRANULAR MATERIAL, TYPE A ON MOLINE ROAD TO BE DONE IN STAGE 2 OR 2A.
  8. INSTALL SUB-BASE GRANULAR MATERIAL, TYPE A ON IL 78 EAST BOUND LANE.
  9. INSTALL ISLAND SPECIAL BASE LEVEL WITH THE SURROUNDING BITUMINOUS BINDER COURSE TO BE DONE IN STAGE 2 OR 2A
  10. INSTALL BITUMINOUS PAVEMENT ON MOLINE RD. TO BE DONE IN STAGE 2 OR 2A.
  11. INSTALL BITUMINOUS PAVEMENT ON IL 78 EAST BOUND LANE.
  12. INSTALL TEMPORARY PAVEMENT ON W. LEG OF IL 78 FROM STA. 482+13.30 TO STA. 488+00.
  13. CUT SWALE FROM STA. 2+97.13 TO CULVERT ON MOLINE ROAD TO BE DONE IN STAGE 2 OR 2A.
- LOCAL TRAFFIC INTO LYNDON WILL HAVE ACCESS USING 3RD ST., BUT SEMI'S WILL NOT BE PERMITTED TO USE 3RD ST.

FILE NAME : c:\projects\226997\226997.dgn  
LEVELS : 1-63  
PLOT SCALE : 1/8"=1'-0"  
PLOT DATE : 08/09/2004  
OPERATOR : DUNCAN - PROGRAM DEVELOPMENT/PLANS
