FAIRFIELD ROAD AT IVANHOE ROAD AND IL. ROUTE 176

TRAFFIC CONTROL PLAN

TRAFFIC CONTROL AND PROTECTION GENERAL NOTES

I. APPLICABLE STANDARDS

701006-02 OFF-RD OPERATIONS, 2L, 2W, 4.5 M (15') TO 600 MM (24") FROM PAVEMENT EDGE

701011-02 OFF-RD MOVING OPERATIONS, 2L, 2W, DAY ONLY

701301-03 LANE CLOSURE, 2L, 2W, SHORT TERM OPERATIONS

701306-02 LANE CLOSURE, 2L, 2W, SLOW MOVING OPERATIONS DAY ONLY, FOR SPEEDS > 45 MPH

701311-03 LANE CLOSURE, 2L, 2W, MOVING OPERATIONS - DAY ONLY

701326-03 LANE CLOSURE, 2L, 2W, PAVEMENT WIDENING, FOR SPEEDS > 45 MPH

701901-01 TRAFFIC CONTROL DEVICES


APPLICABLE DETAILS

LC 7002 2L, 2W, OFF ROAD OPERATIONS, DAY ONLY OPERATION

LC 7003 2L, 2W UNDIVIDED, LANE CLOSURE - DAY OR NIGHT

LC 7006 SIDEROADS, INTERSECTIONS, DRIVEWAYS

- 2. THE PERMANENT TRAFFIC CONTROL DEPICTED HEREON IS THE MINIMUM REQUIREMENT. ADDITIONAL TRAFFIC CONTROL DEVICES AS SPECIFIED BY THE ABOVE HIGHWAY STANDARDS AND THE SPECIAL PROVISIONS SHALL BE PLACED BY THE CONTRACTOR TO THE SATISFACTION OF THE ENGINEER. ALL TRAFFIC CONTROL DEVICES SHALL BE CONSIDERED INCIDENTAL TO THE LUMP SUM PAY ITEM "TRAFFIC CONTROL AND PROTECTION" UNLESS OTHERWISE INDICATED IN THE PLANS OR SPECIAL PROVISIONS.
- 3. ALL TRAFFIC CONTROL WARNING SIGNS AND ASSOCIATED SIGNING MOUNTED WITH THE WARNING SIGNS SHALL HAVE BLACK LEGENDS AND BORDERS ON FLUORESCENT ORANGE REFLECTIVE SHEETING.
- 4. ALL CONSTRUCTION SIGNS, BARRICADES AND OTHER DEVICES REQUIRED TO CONTROL TRAFFIC SHALL BE FURNISHED, INSTALLED AND MAINTAINED BY THE CONTRACTOR.
- 5. ALL TRAFFIC CONTROL DEVICES SHALL BE REMOVED, COVERED OR TURNED AWAY FROM TRAFFIC IMMEDIATELY WHEN THEY ARE NO LONGER NECESSARY, WHEN A SIGN IS COVERED, IT'S POST SHALL HAVE A REFLECTIVE 3 INCH x 6 INCH DELINEATOR INSTALLED.
- 6. THE SIGN SPACING FOR THE ABOVE HIGHWAY STANDARDS SHALL BE IN ACCORDANCE WITH THE SIGN SPACING TABLE SHOWN HEREIN THIS TRAFFIC CONTROL PLAN.
- 7. ROAD NAME PLATES SHALL BE INSTALLED ON THE "ROAD WORK AHEAD" SIGNS AT THE INTERSECTIONS SHOWN IN THIS TRAFFIC CONTROL PLAN. THE ROAD NAME PLATES SHALL BE 9 INCH BLANKS WITH 6 INCH UPPERCASE AND 5 INCH LOWERCASE LETTERING. THE ROAD NAME PLATES SHALL BE FURNISHED BY THE CONTRACTOR.
- 8. 'ROAD WORK AHEAD' SIGNS SHALL BE EQUIPPED WITH MONODIRECTIONAL TYPE A AMBER FLASHING LIGHTS.

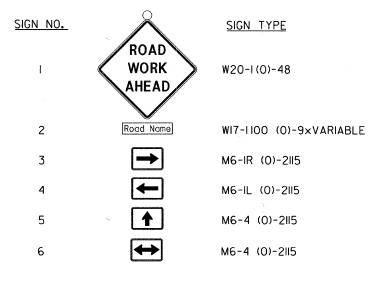

POSTED SP	EED LIMIT
FAIRFIELD ROAD: 45 MPH	
IVANHOE ROAD: 35MPH	
IL. ROUTE 176:55 MPH	
TRAFFIC CON	ITROL SIGN
SPACING TABLE	
55 MPH	500 FT.
45-50 MPH	350 FT.
<45 MPH	200 FT.

