




F.A.U. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
2697	3363 RS-1	COOK	36	19
STA. 34+56		TO STA. 44+02		
FED. ROAD DIST. NO. 1		ILLINOIS FED. AID PROJECT		
CONTRACT NO. 62706				

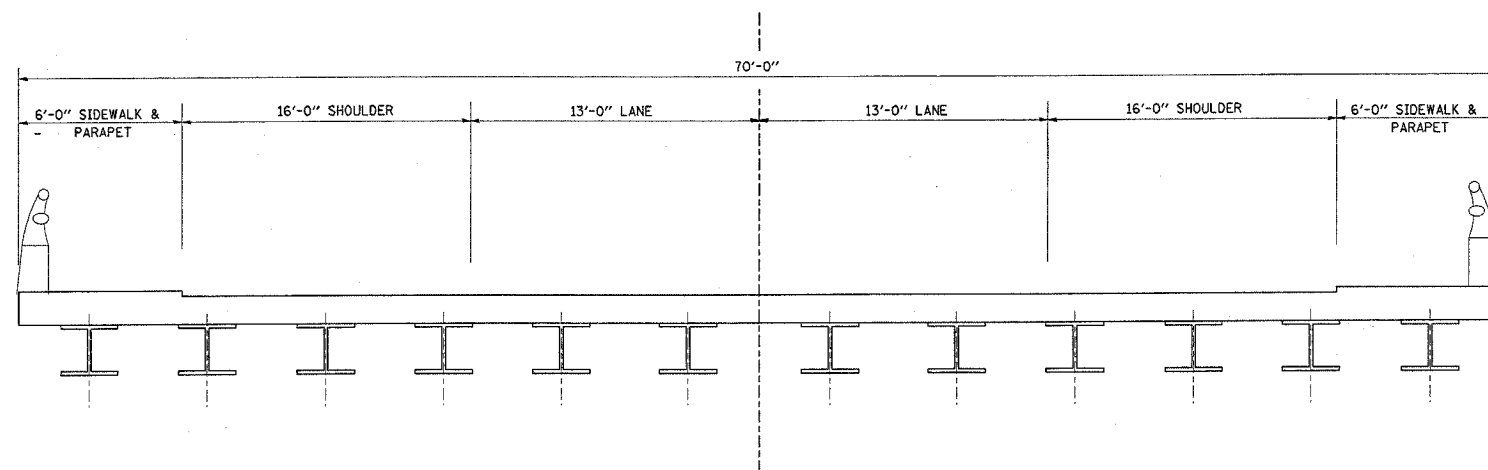

WILLOW SPRINGS RD. OVER I-55 EXPRESSWAY

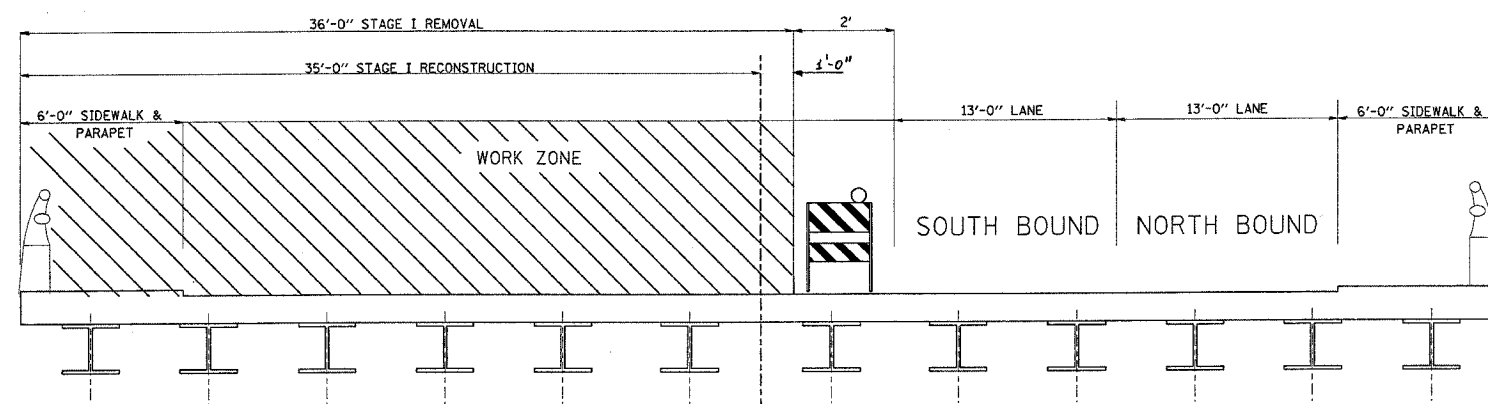

LOOKING NORTH
STAGE I

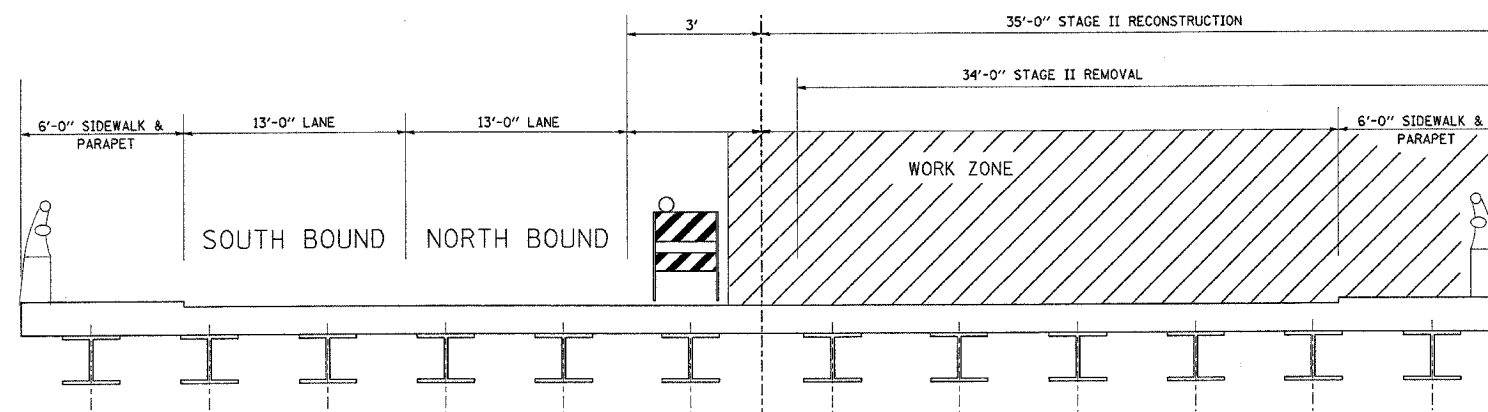

LOOKING NORTH
STAGE II

 INDICATES WORK AREA

GENERAL NOTES

PLAN DIMENSIONS AND DETAILS RELATIVE TO THE EXISTING STRUCTURE HAVE BEEN TAKEN FROM EXISTING PLANS AND ARE SUBJECT TO NOMINAL CONSTRUCTION VARIATIONS. IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO VERIFY SUCH DIMENSION AND DETAILS IN THE FIELD AND MAKE NECESSARY APPROVED ADJUSTMENTS PRIOR TO CONSTRUCTION OR ORDERING OF MATERIALS. SUCH VARIATION SHALL NOT BE CAUSE FOR ADDITIONAL COMPENSATION FOR A CHANGE IN THE SCOPE OF WORK, HOWEVER, THE CONTRACTOR WILL BE PAID FOR THE ACTUAL QUANTITY FURNISHED AT THE UNIT BID PRICE FOR THE WORK.

ALL STRUCTURAL STEEL SHALL CONFORM TO AASHTO CLASSIFICATION M-270, GR.36 UNLESS OTHERWISE SPECIFIED.

REINFORCEMENT BARS SHALL CONFORM TO THE REQUIREMENTS OF AASHTO M-31, M-322 GRADE 60.

ALL STRUCTURAL STEEL SHALL BE SHOP PAINTED WITH THE INORGANIC ZINC RICH PRIMER PER AASHTO M 300, TYPE 1. COST INCLUDED WITH BRIDGE JOINT SYSTEM (EXPANSION), 1-5/8".

JOINT OPENINGS SHALL BE ADJUSTED ACCORDING TO ARTICLE 503.10 (c) OF THE STANDARD SPECIFICATION WHEN THE DECK IS POURED AT AN AMBIENT TEMPERATURE OTHER THAN 50°F

SN 016-0537 HAS A 5°-12'-25" SKEW TO THE NORTH THAT IS NOT SHOWN IN THE PLANS

REVISIONS		ILLINOIS DEPARTMENT OF TRANSPORTATION	
NAME	DATE		
		TYPICAL CROSS SECTIONS FOR TRAFFIC CONTROL DETAILS WILLOW SPRINGS SN 016-0537	
SCALE:	VERT. NONE HORIZ. NONE	DRAWN BY S.E.S.	
DATE	8/25/2004	CHECKED BY	
