F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
22	16R	WHITESIDE	201	69
STA.	TO STA.			
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

CONTRACT NO. 64656

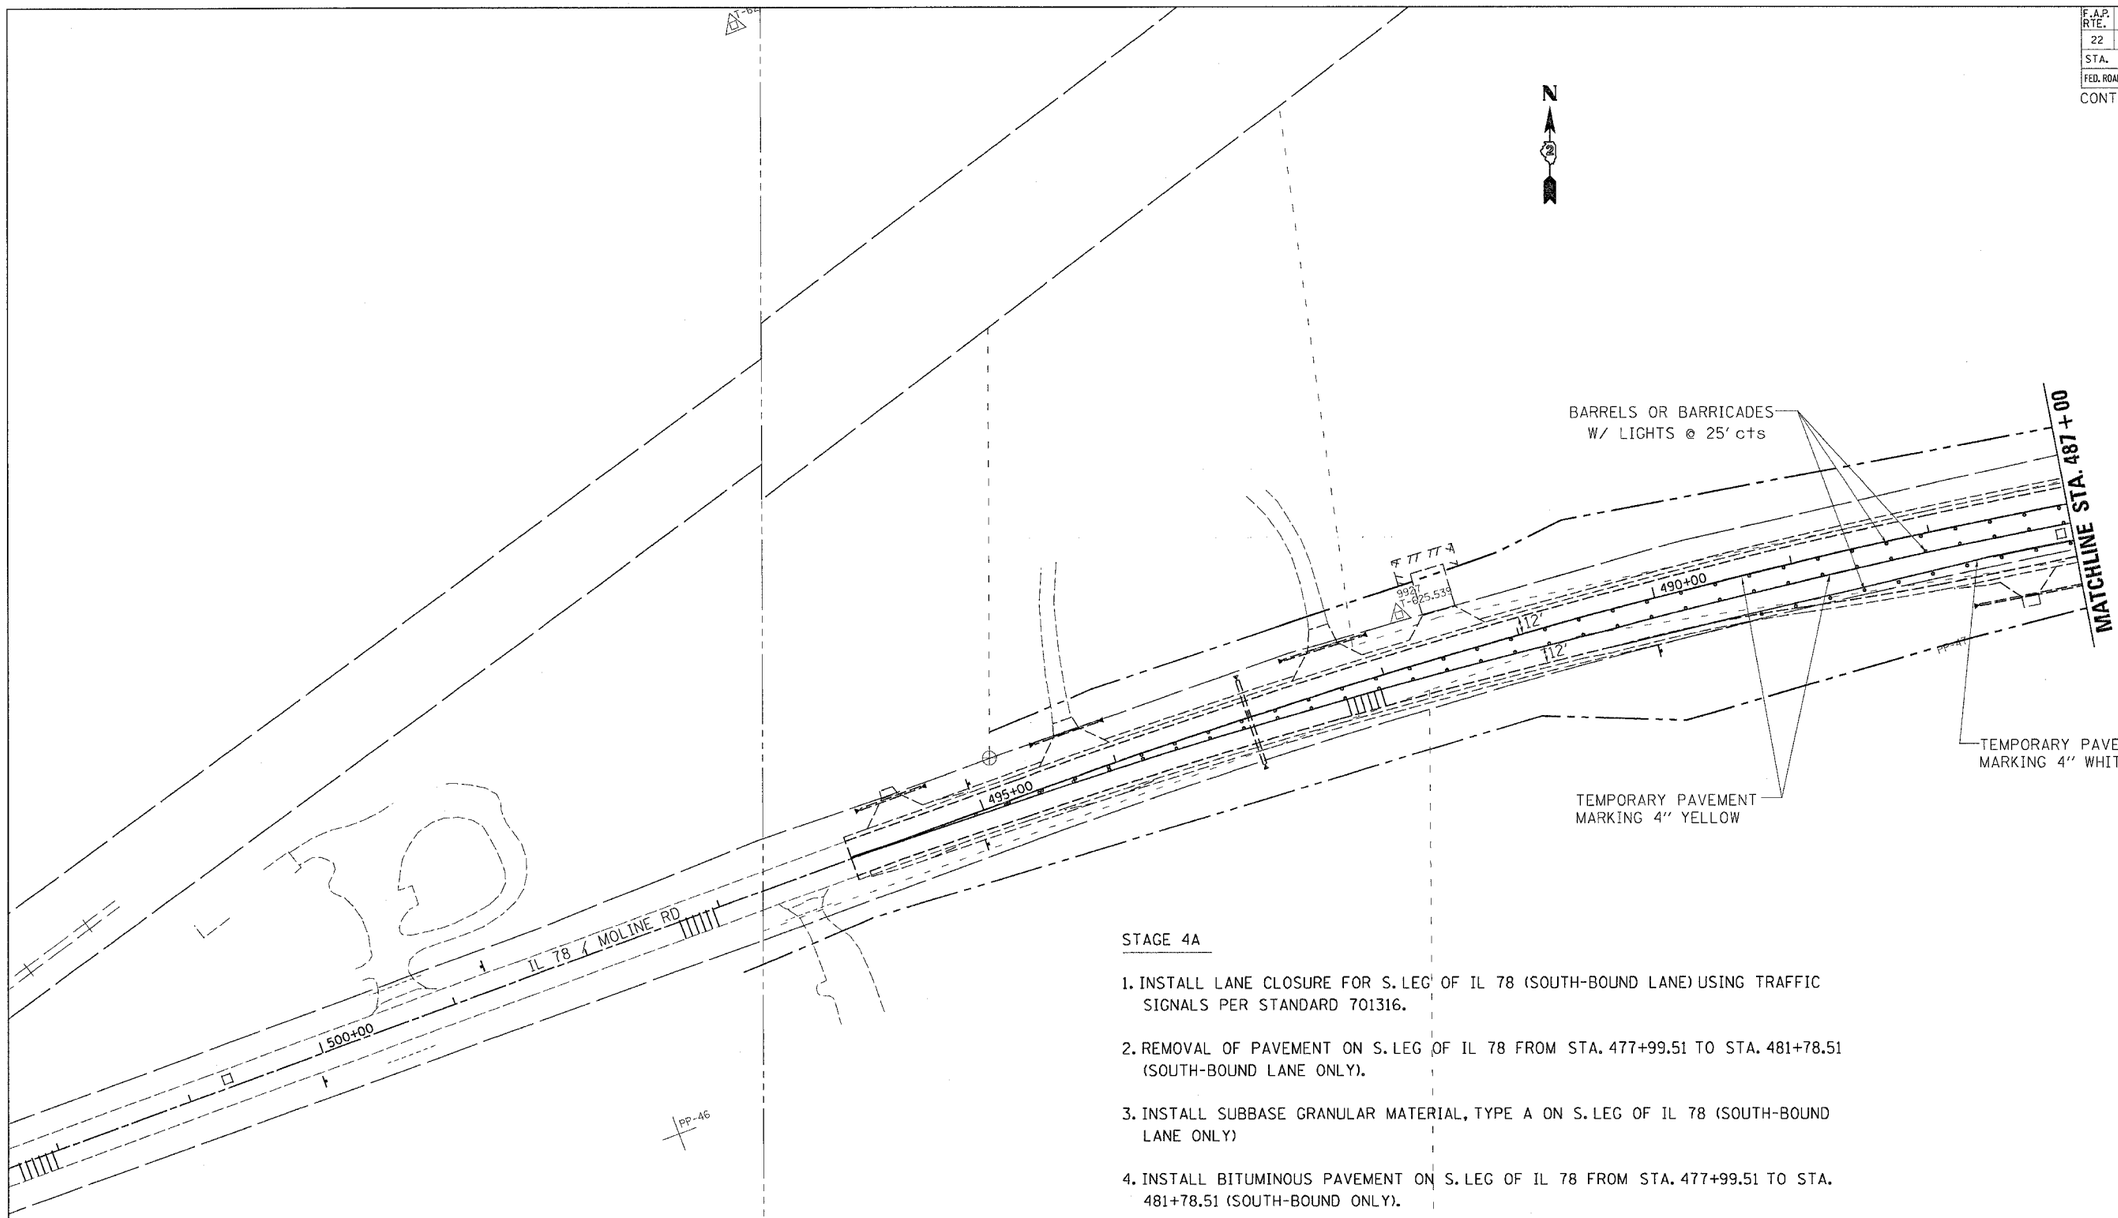

NOTE:

USE SAME SIGNAL AND SIGNAGE PLACEMENTS AS IN STAGE 4.

STAGE 4A

1. INSTALL LANE CLOSURE FOR S. LEG OF IL 78 (SOUTH-BOUND LANE) USING TRAFFIC SIGNALS PER STANDARD 701316.
2. REMOVAL OF PAVEMENT ON S. LEG OF IL 78 FROM STA. 477+99.51 TO STA. 481+78.51 (SOUTH-BOUND LANE ONLY).
3. INSTALL SUBBASE GRANULAR MATERIAL, TYPE A ON S. LEG OF IL 78 (SOUTH-BOUND LANE ONLY)
4. INSTALL BITUMINOUS PAVEMENT ON S. LEG OF IL 78 FROM STA. 477+99.51 TO STA. 481+78.51 (SOUTH-BOUND ONLY).
5. REMOVE LANE CLOSURE FOR S. LEG OF IL 78 (SOUTH-BOUND LANE).
6. INSTALL LANE CLOSURE AT INTERSECTION OF MOLINE RD AND IL 78 PER STANDARD 701701 PAID FOR AS 701316.
7. FINISH CONSTRUCTING ISLAND SPECIAL AT THE INTERSECTION OF MOLINE ROAD AND IL 78, (BASE WAS POURED IN STAGE 2).
8. REMOVE ROAD CLOSURE ON 3RD ST AND ALL SIGNAGE.
9. REMOVE ALL SIGNALS AND SIGNAGE FOR STAGE 4A.

REMOVE EXISTING PAVEMENT

FILE NAME = c:\dgn-projects\v22859917\d0859917sg4a.dgn
LEVELS = 1,63
PLOT SCALE = 1.0000 '/ IN. (SEE PLOTSCALE)
PLOT DATE = Mon Apr 12 10:58:01 2004
OPERATOR = DUNCAN - PROGRAM DEVELOPMENT/PLANS

STAGE 4A
