


FAS RTE	SECTION	COUNTY	TOTAL SHEETS	SHEET NO
939	*	PULASKI	29	12
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	
* D-9 CONT MAINT FY 04-1 0098814				

LEGEND


TT TYPE III BARRICADE

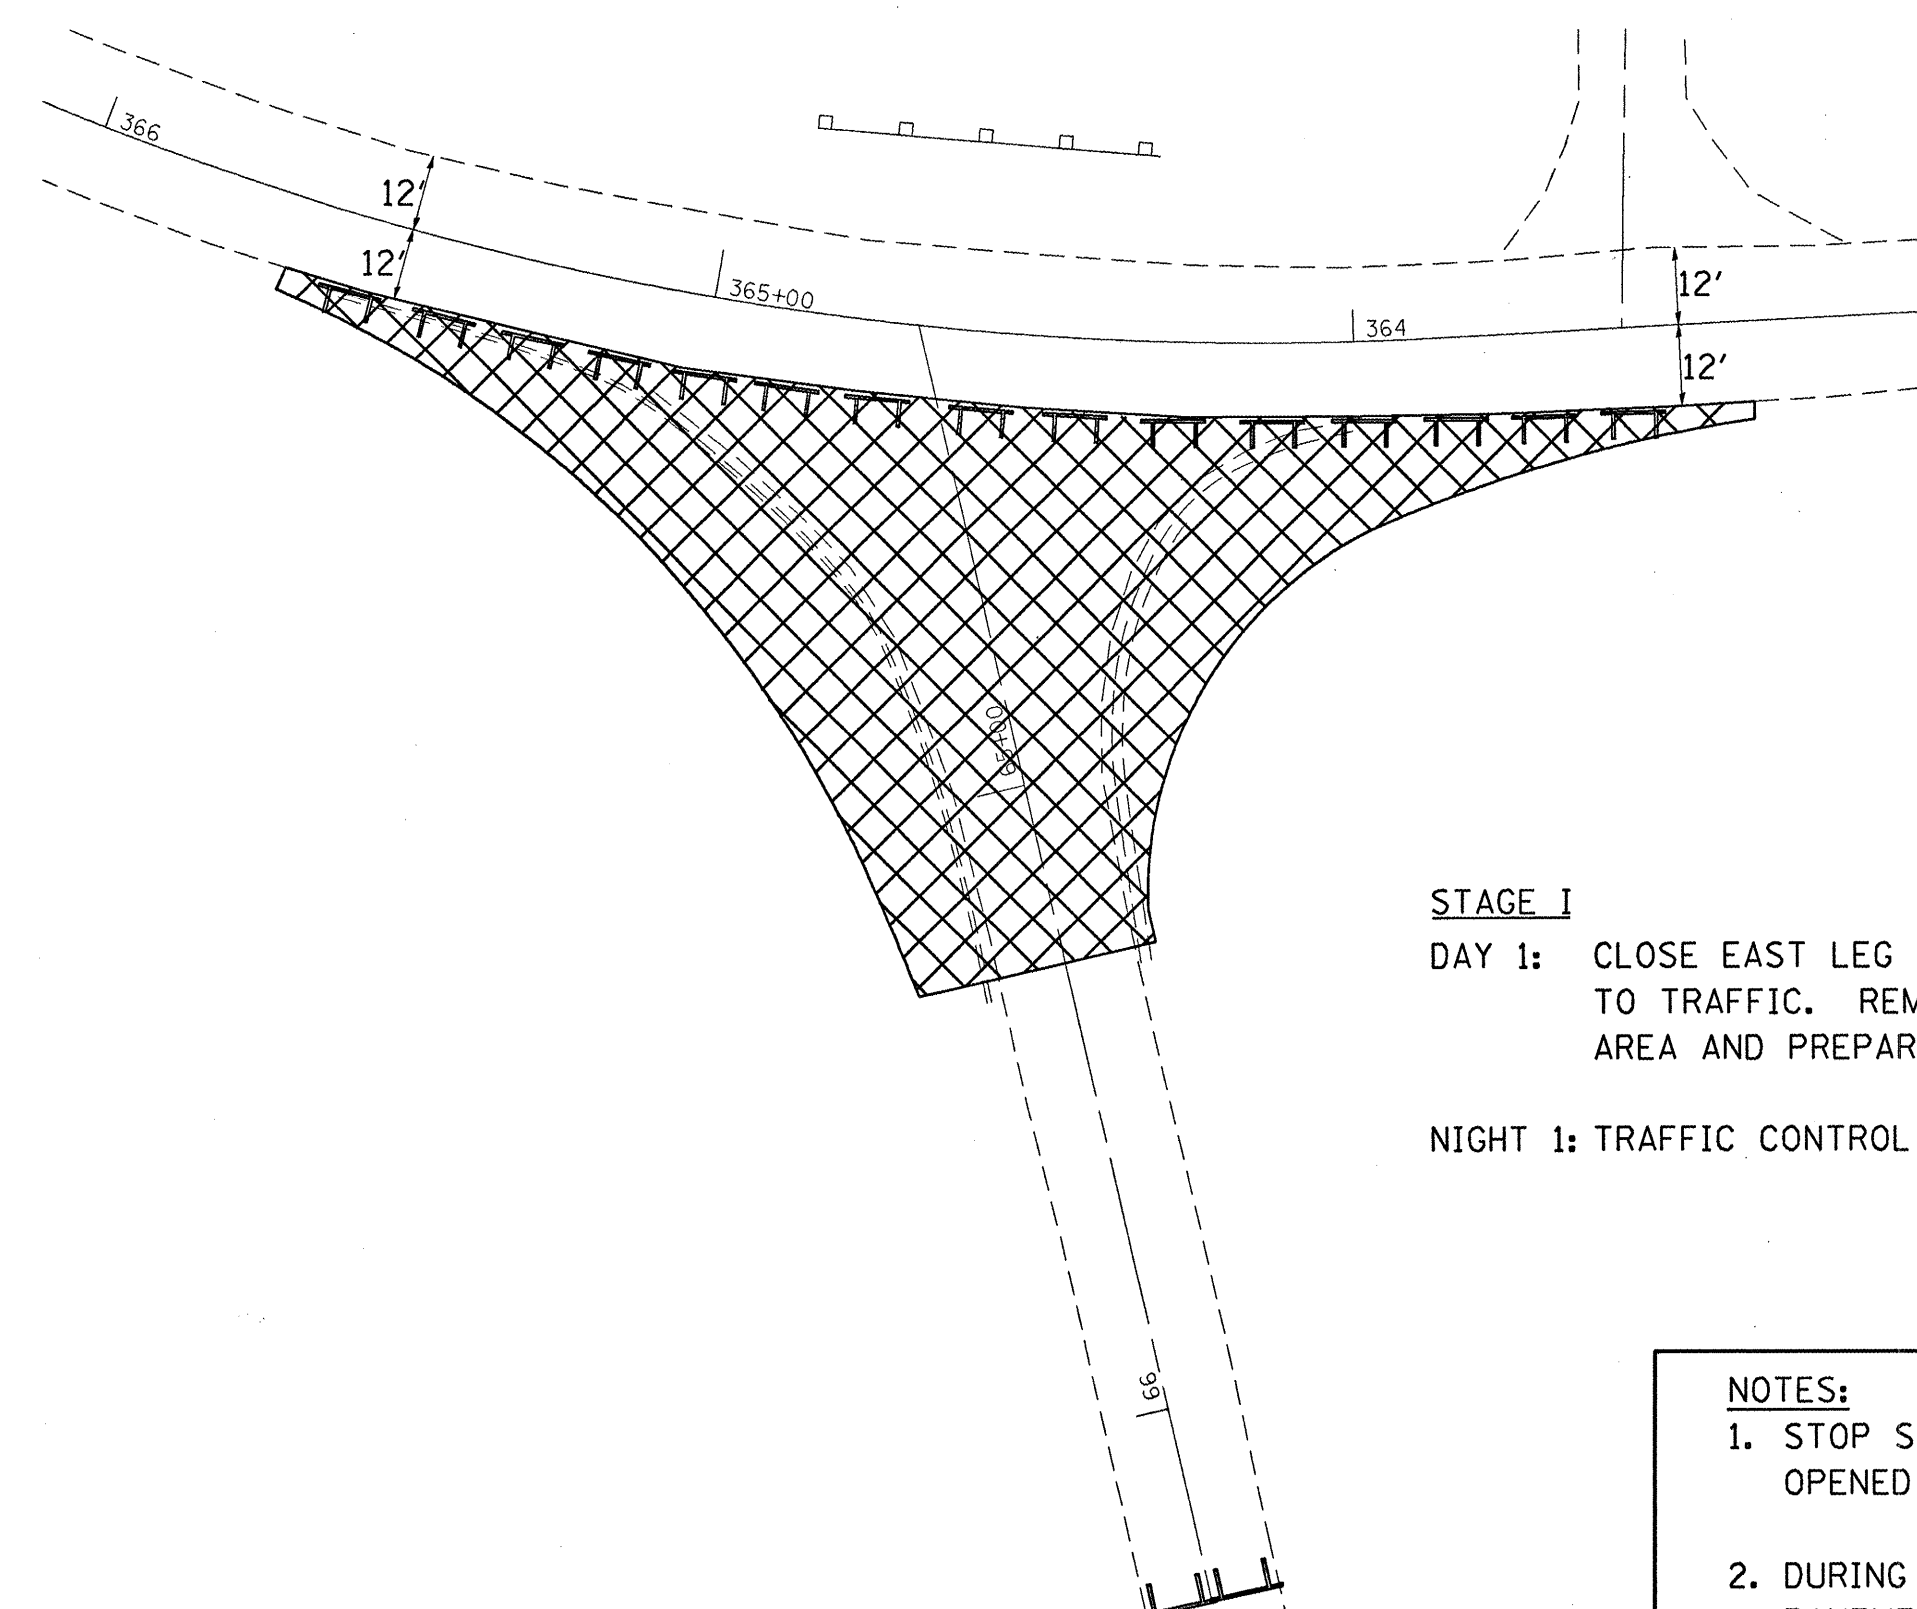

STAGE I

DAY 1: CLOSE EAST LEG OF INTERSECTION TO TRAFFIC. REMOVE CROSSHATCHED AREA AND PREPARE SUBGRADE.

NIGHT 1: TRAFFIC CONTROL SURVEILLANCE

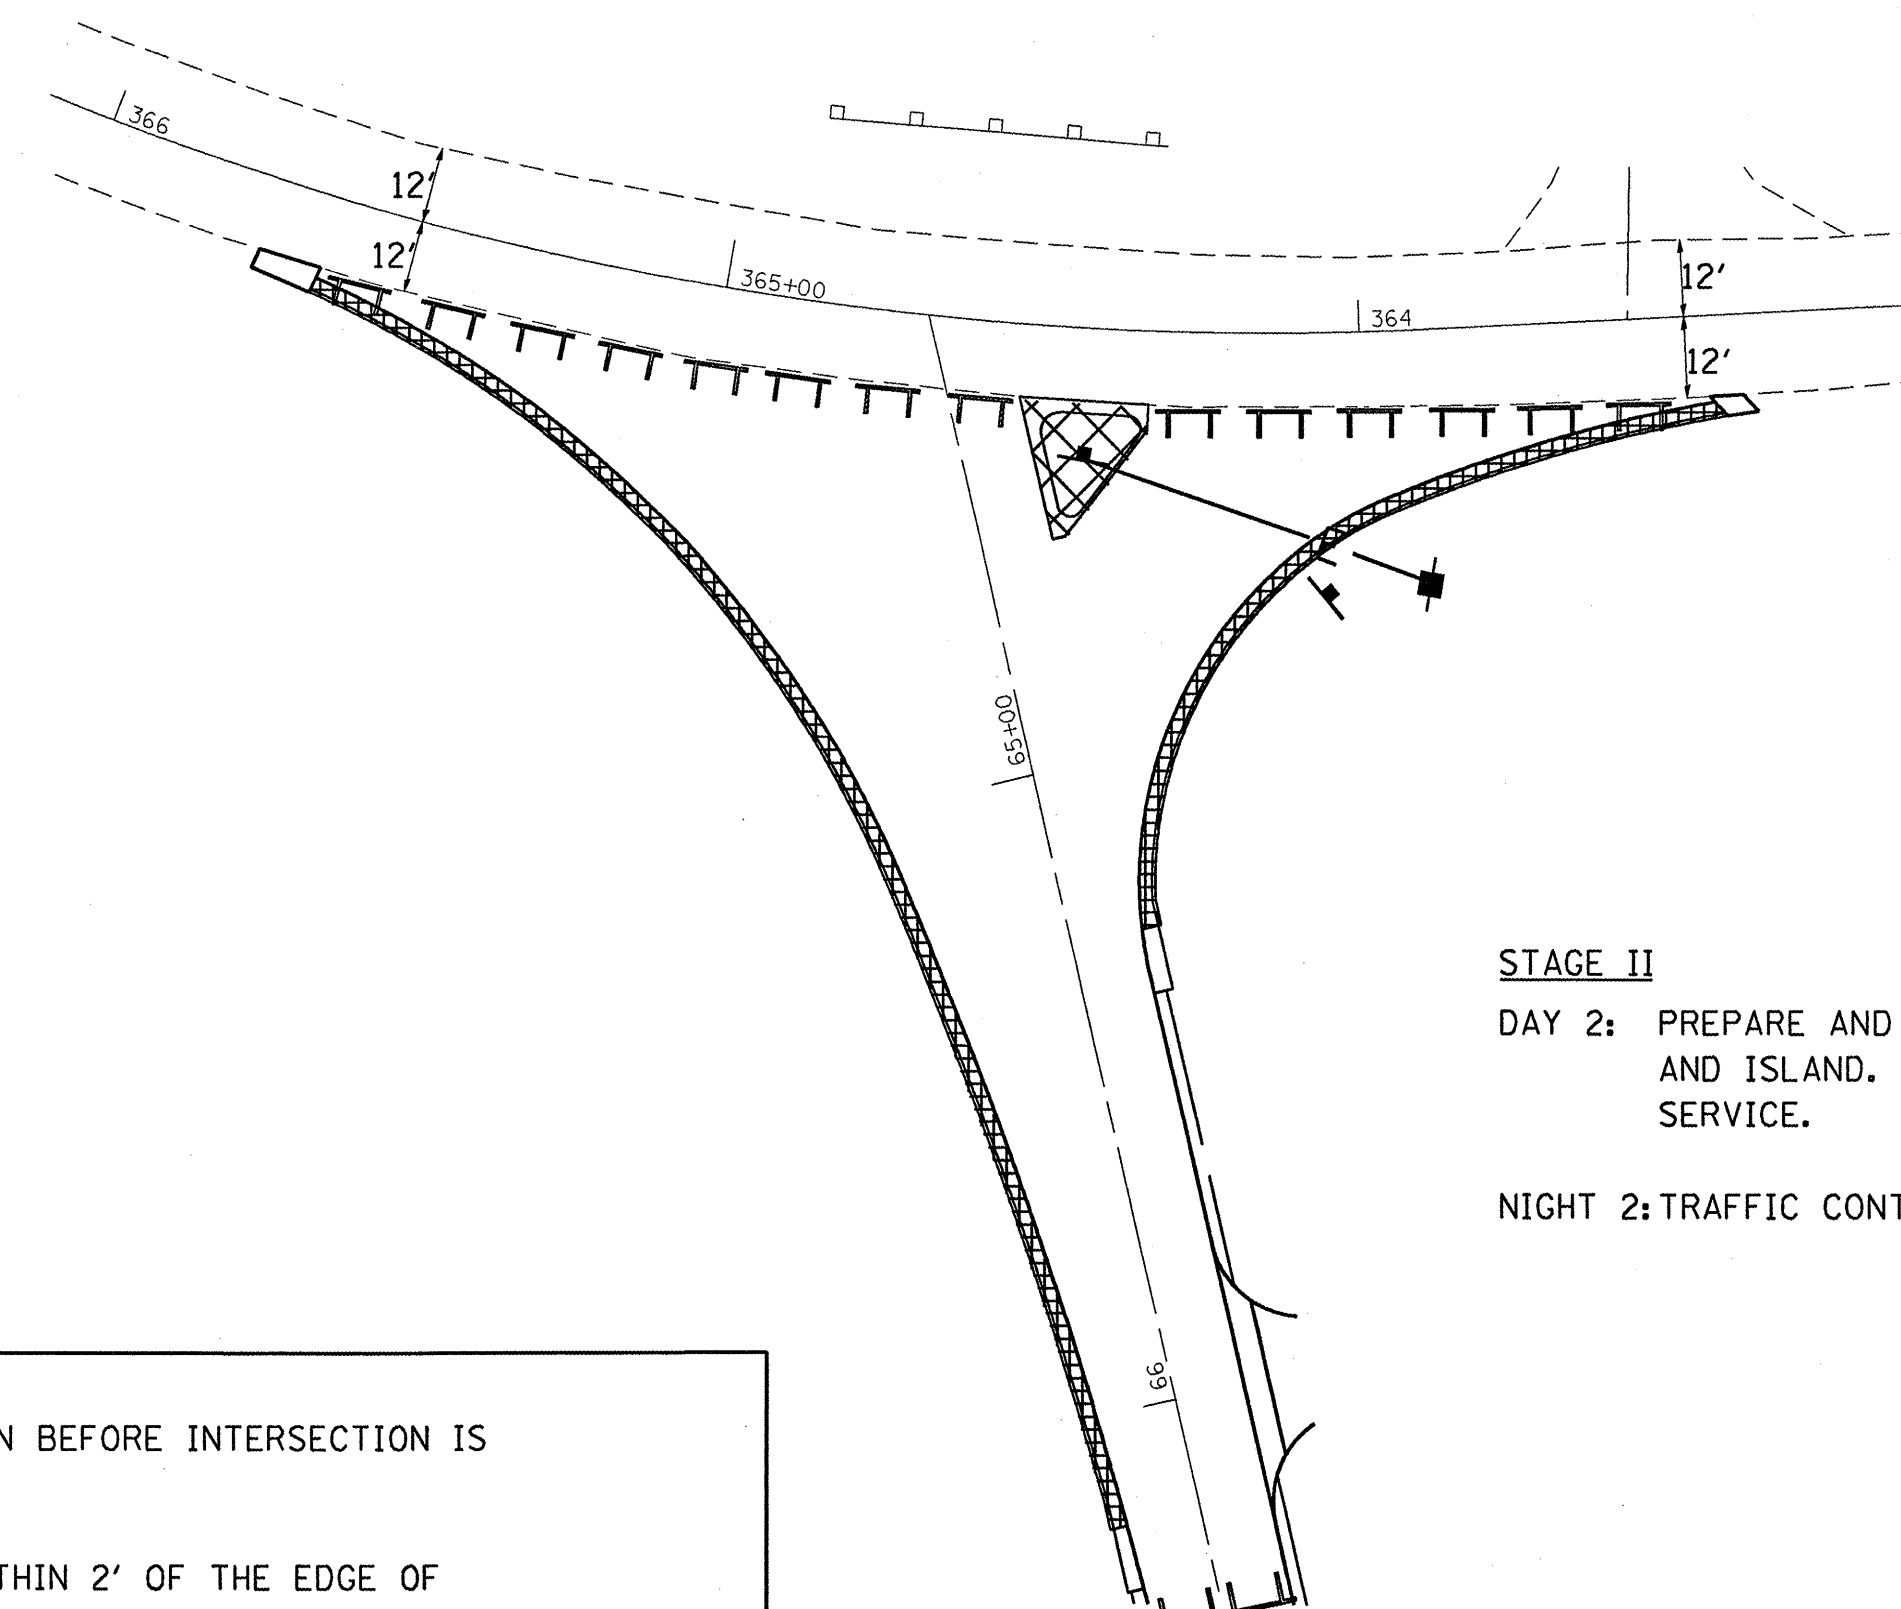


STAGE II

DAY 2: PREPARE AND POUR CURB AND GUTTER AND ISLAND. INSTALL NEW ELECTRIC SERVICE.

NIGHT 2: TRAFFIC CONTROL SURVEILLANCE.

NOTES:

1. STOP SIGN AND FLASHING BEACON SHALL BE RELOCATED AND IN OPERATION BEFORE INTERSECTION IS OPENED TO TRAFFIC.
2. DURING DAYTIME OPERATIONS WHEN WORKERS OR ACTIVITIES ENCROACH WITHIN 2' OF THE EDGE OF PAVEMENT OF OLD US 51, TRAFFIC ON OLD US 51 SHALL BE MAINTAINED ON THE SOUTHBOUND LANE AND CONTROLLED WITH A FLAGGER (STANDARD 701201).
3. ON NIGHTS 3, 4, & 5, BOARDS SHALL BE ERECTED OVER THE NEW CONCRETE PAVEMENT TO SUPPORT THE TYPE III BARRICADES. ANY DAMAGE TO THE NEW PCC PAVEMENT SHALL BE REPAIRED AT THE THE CONTRACTOR'S EXPENSE.

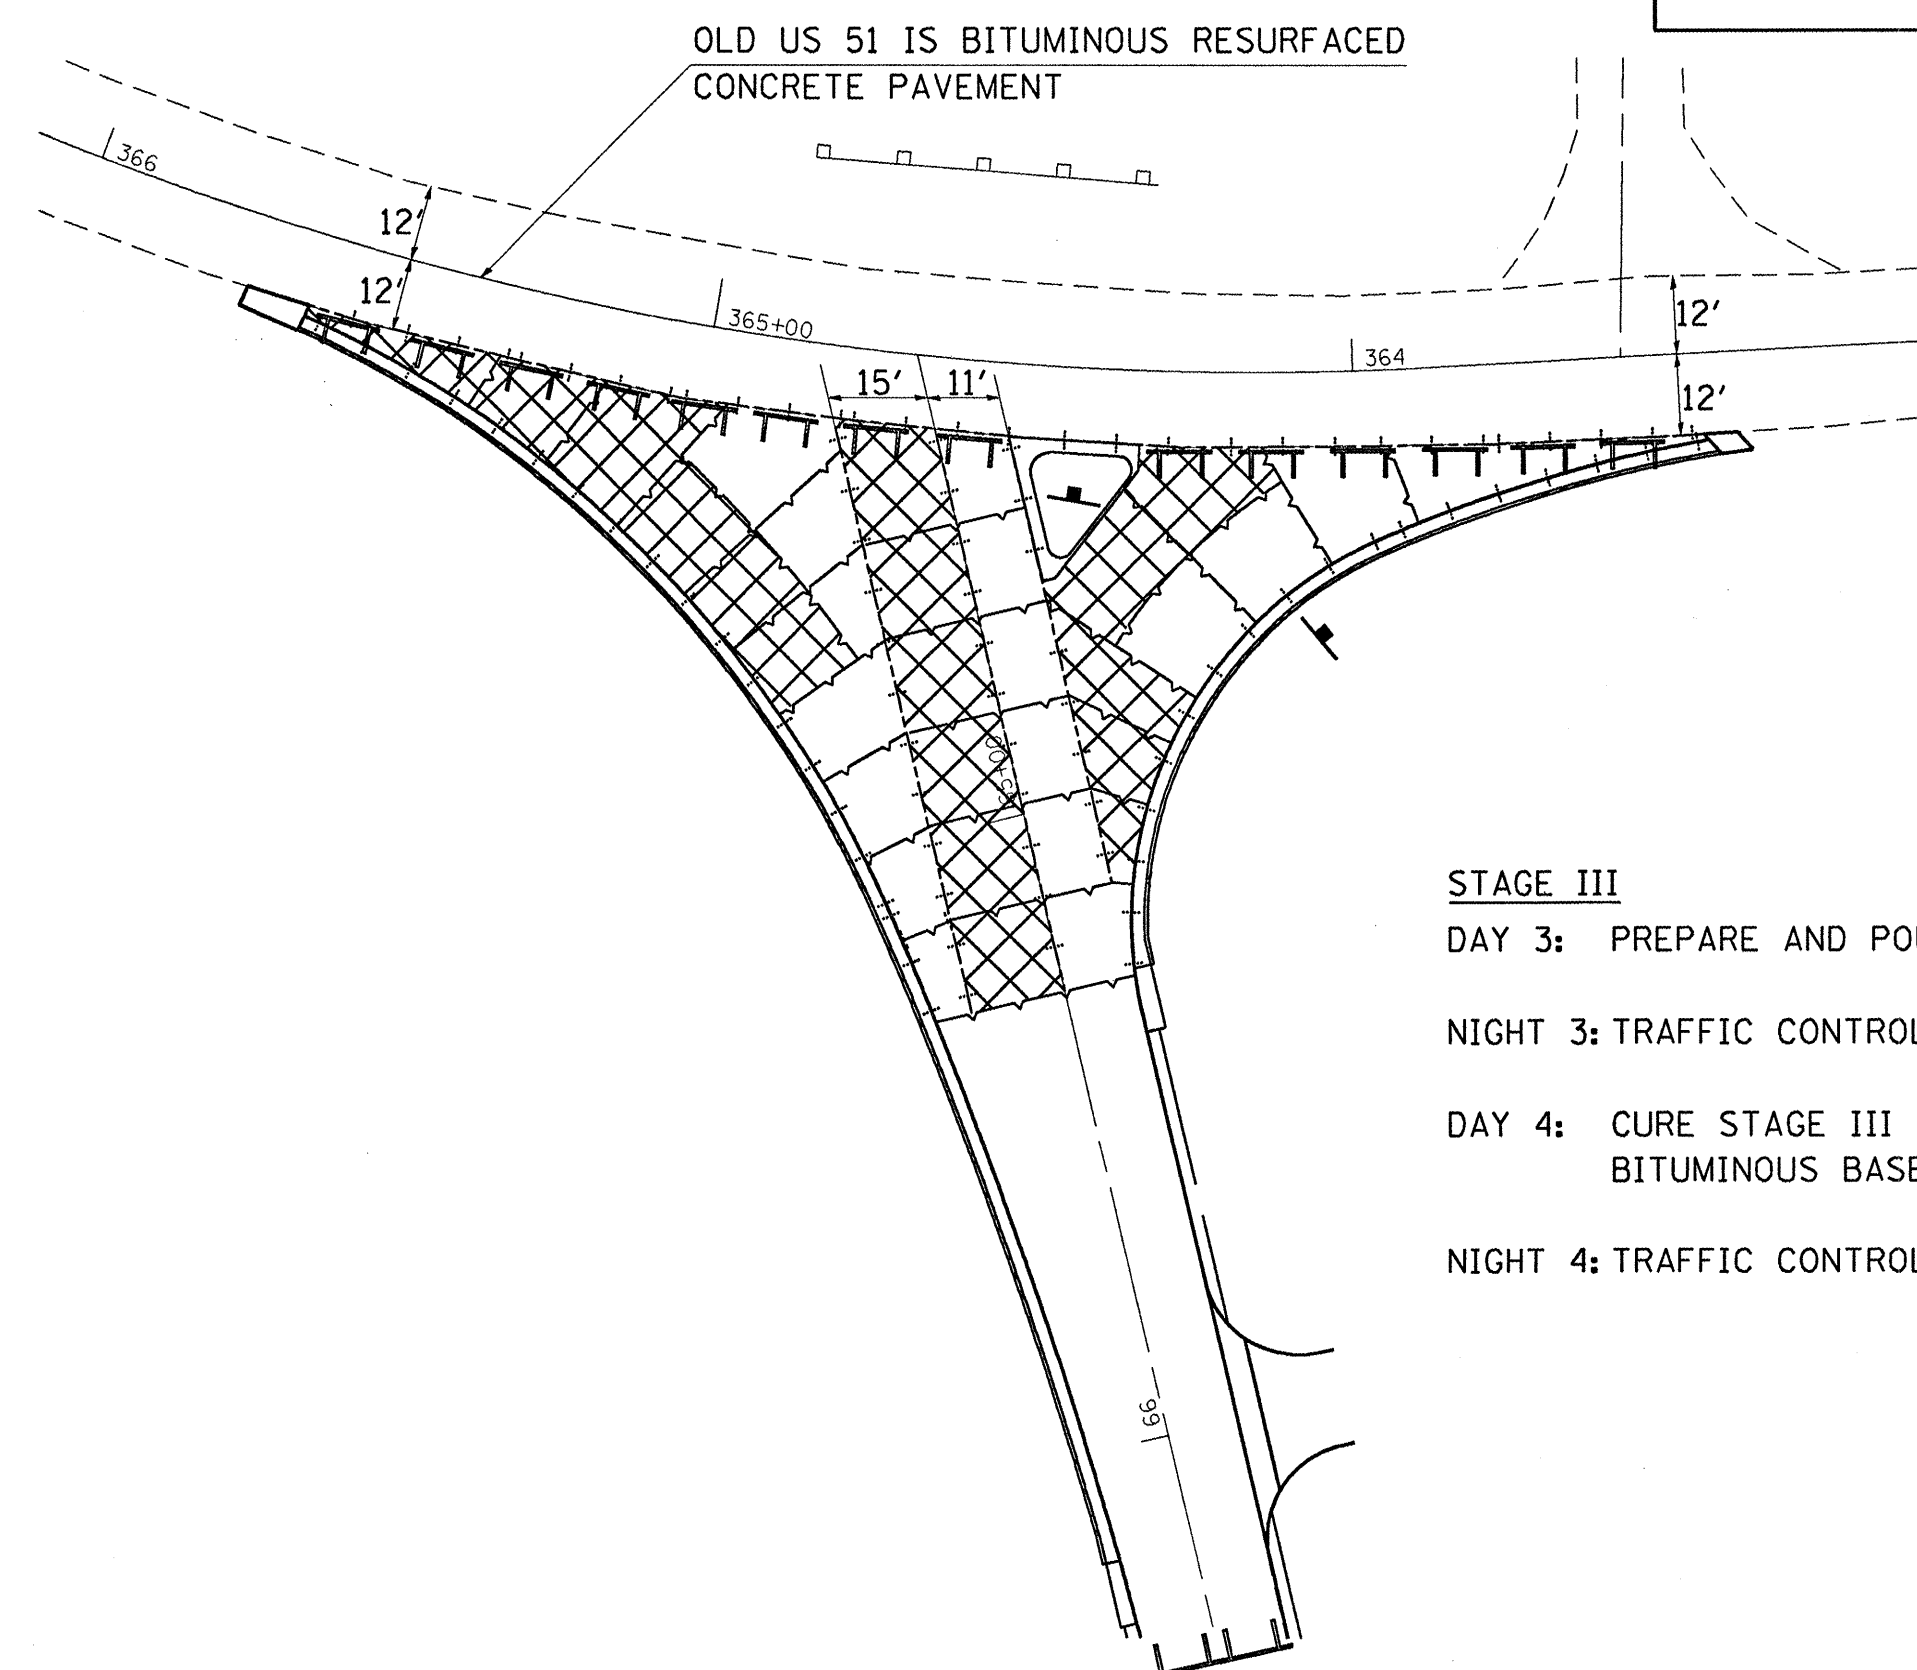


STAGE III

DAY 3: PREPARE AND POUR CROSSHATCHED AREA.

NIGHT 3: TRAFFIC CONTROL SURVEILLANCE.

DAY 4: CURE STAGE III PAVEMENT. PLACE BITUMINOUS BASE COURSE.


NIGHT 4: TRAFFIC CONTROL SURVEILLANCE.

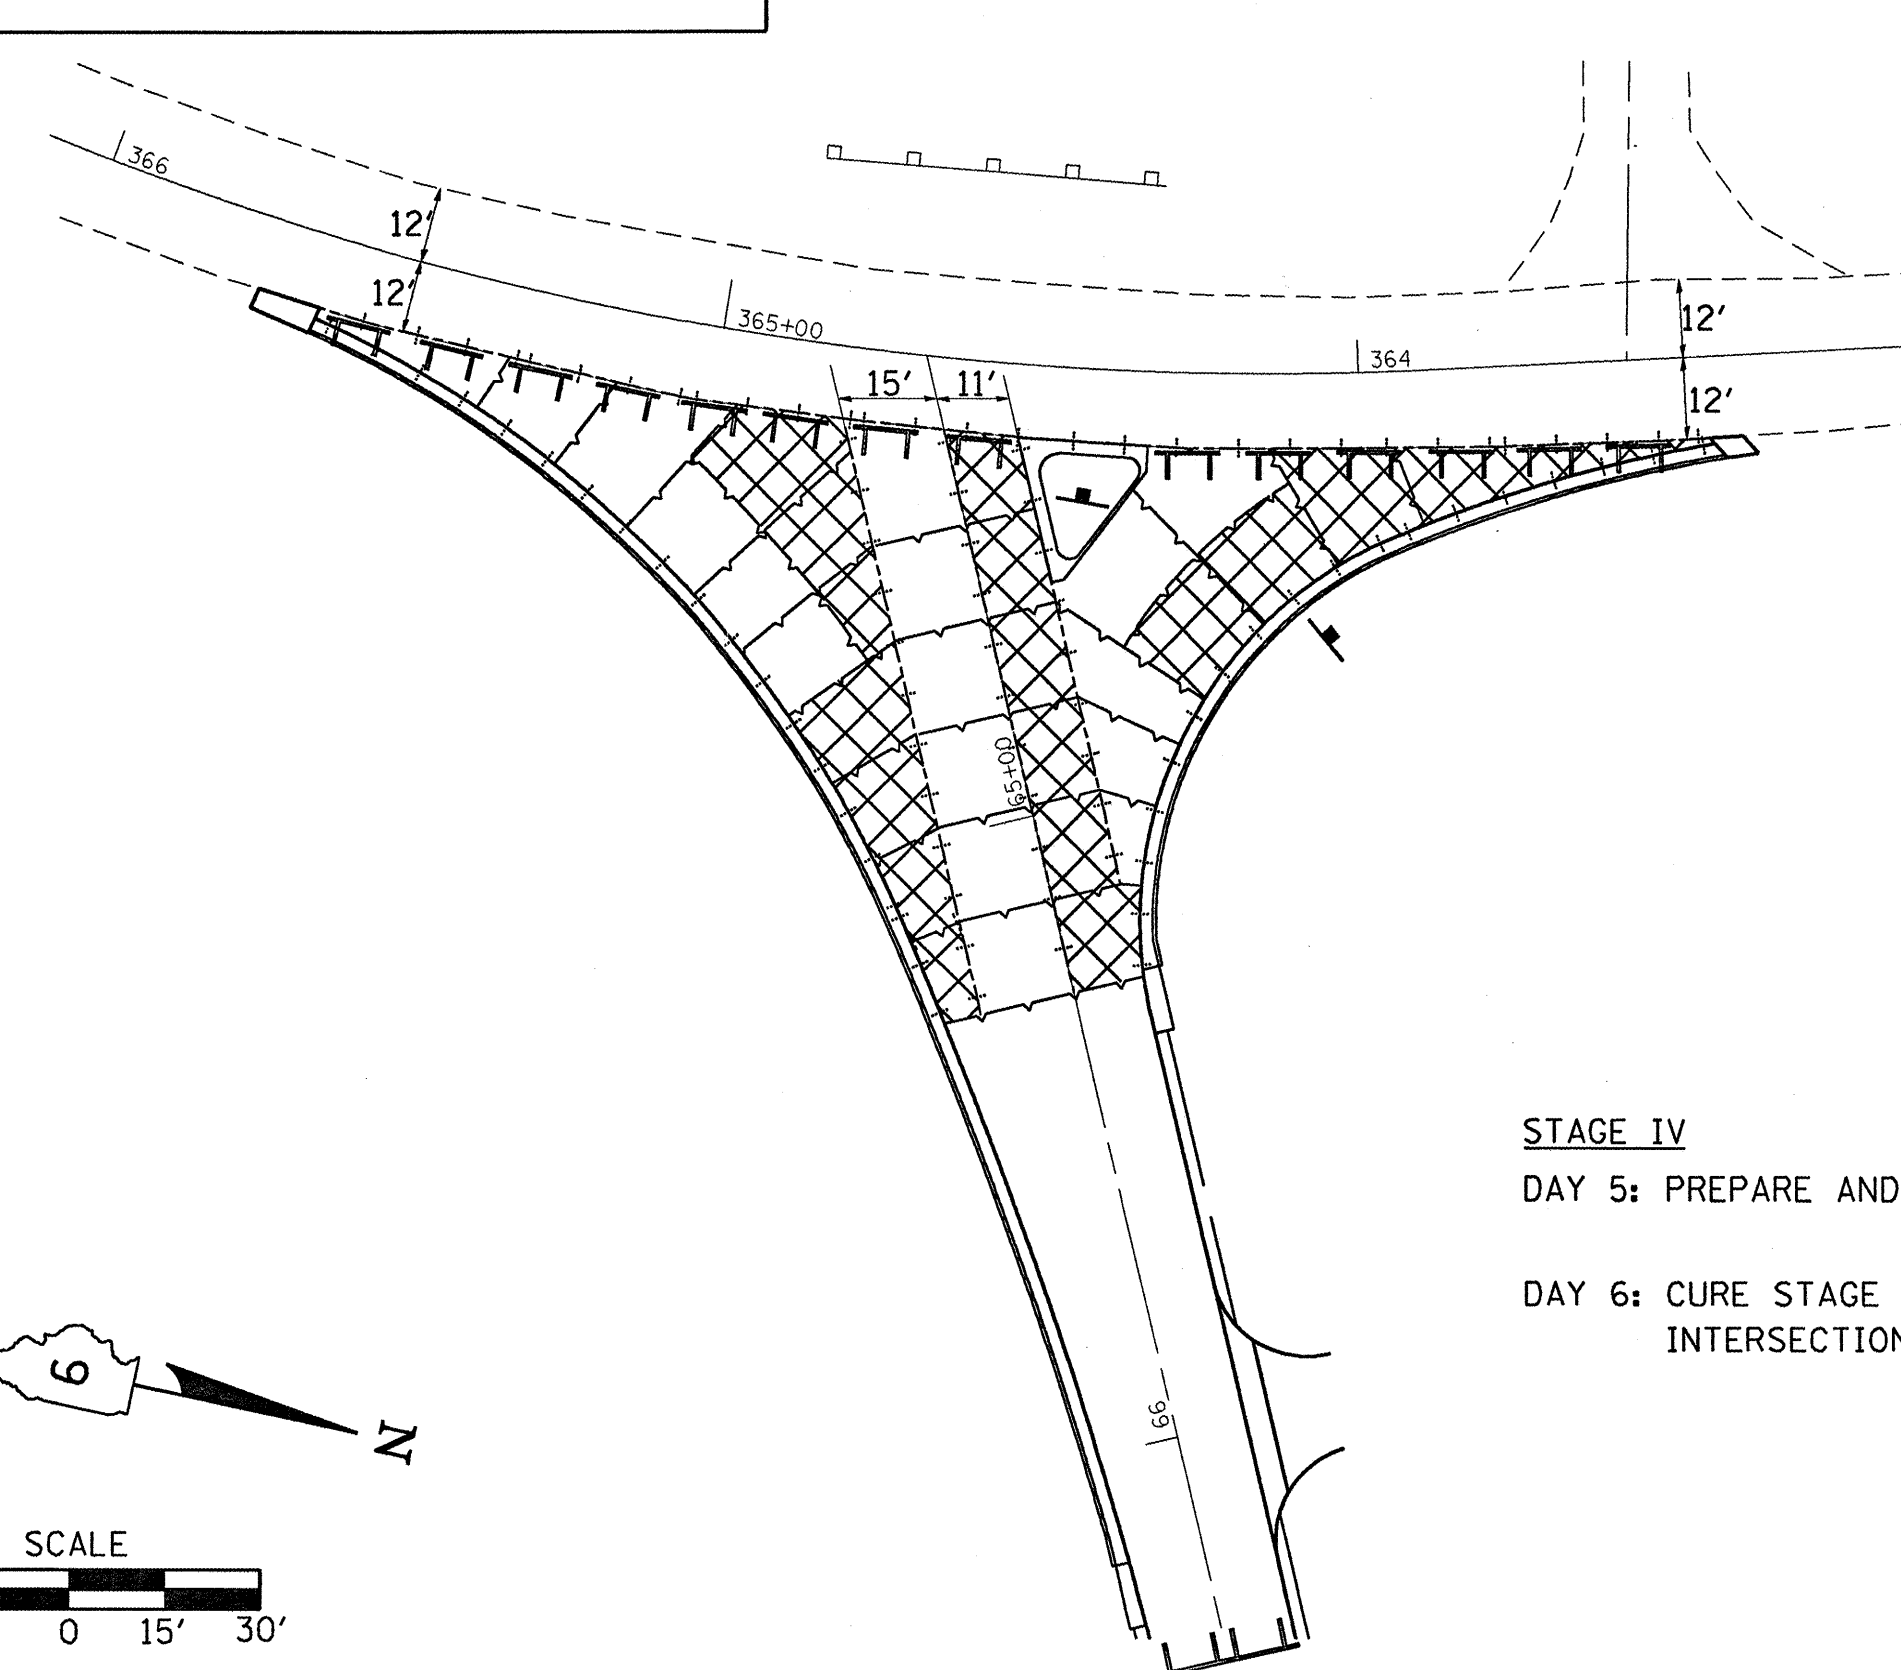

STAGE IV

DAY 5: PREPARE AND POUR CROSSHATCHED AREA.

DAY 6: CURE STAGE IV PAVEMENT. OPEN INTERSECTION TO TRAFFIC.

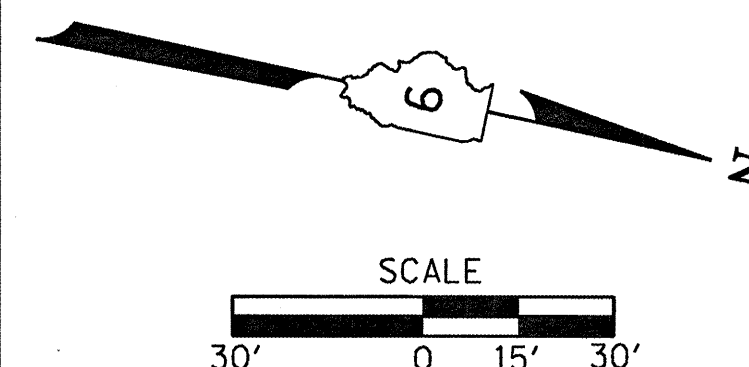

SUGGESTED STAGE CONSTRUCTION PLAN
