





F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
331	*	**	93	53
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	
* (1-4)RS,(1-3)RS-1				
** JACKSON/WILLIAMSON				

9878

98783

## STAGE 2

1. CLOSE EB IL 13 PASSING LANE AND LT. TURN LANE.
2. WB IL 13 LT. TURN LANE REMAINS CLOSED.
3. OPEN SOUTH DIVISION STREET TO RIGHT IN / RIGHT OUT OFF OF IL 13.
4. SHIFT BOTH WB IL 13 LANES TO THE NORTH BY 3'.
5. LIMIT TRAFFIC ON NORTH DIVISION TO RIGHT IN / RIGHT OUT OFF OF IL 13.
6. REMOVE EXISTING PAVEMENT AND CONSTRUCT NEW PCC PAVEMENT AS CROSS HATCHED.
7. REMOVE EXISTING BITUMINOUS SHOULDER AS SHOWN AND CONSTRUCT NEW BITUMINOUS SHOULDER.

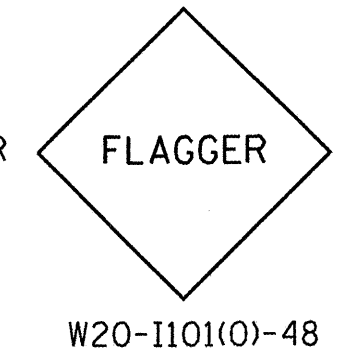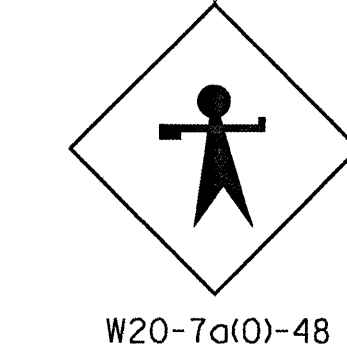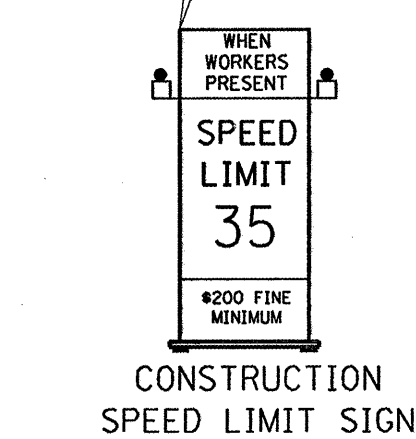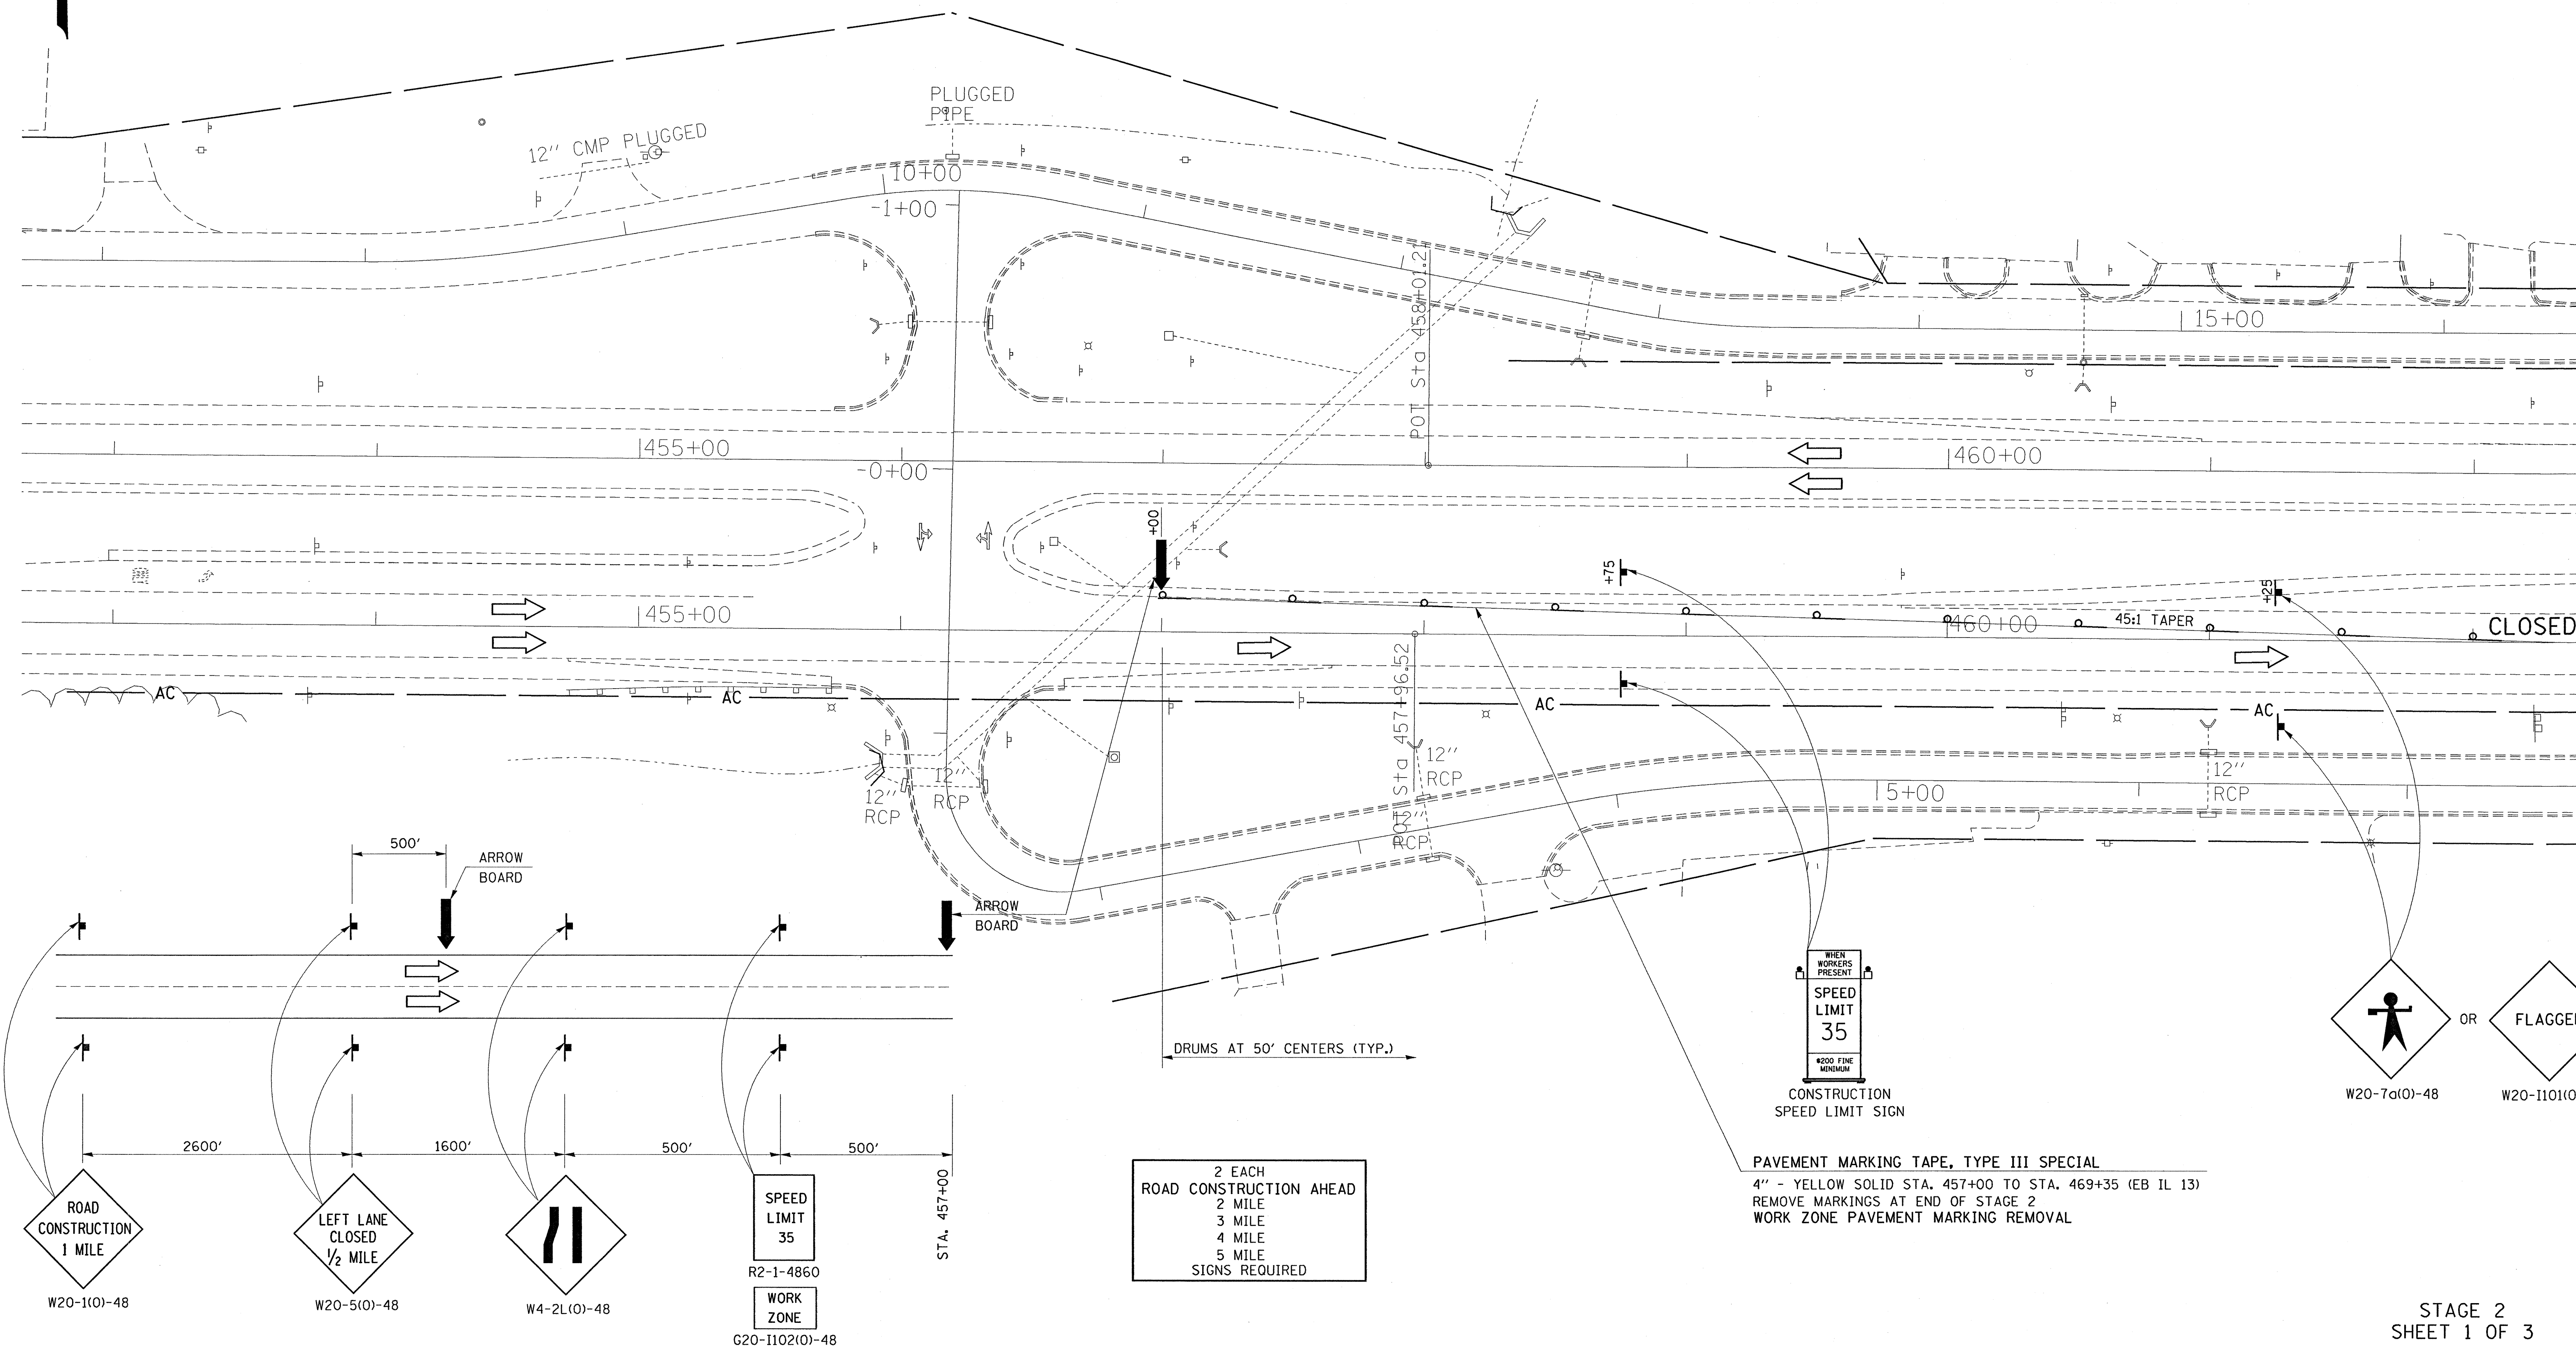

PAVEMENT MARKING TAPE, TYPE III SPECIAL  
4" - YELLOW SOLID STA. 457+00 TO STA. 469+35 (EB IL 13)  
REMOVE MARKINGS AT END OF STAGE 2  
WORK ZONE PAVEMENT MARKING REMOVAL

2 EACH  
ROAD CONSTRUCTION AHEAD  
2 MILE  
3 MILE  
4 MILE  
5 MILE  
SIGNS REQUIRED

SPEED  
LIMIT  
35  
R2-1-4860  
WORK  
ZONE  
G20-1102(0)-48

STAGE 2  
SHEET 1 OF 3
