

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
*	**	MACOUPIN	231	76
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	
• FAP 325 & FAP 604 •• 14R; 115RS-2; 116RS-4; 101RS-2				

**TRAFFIC CONTROL AND PROTECTION**



**STAGE 3 NOTES**

1. THIS TRAFFIC CONTROL PLAN SHALL BE USED IN CONJUNCTION WITH THE APPLICABLE TRAFFIC CONTROL STANDARDS, AND AS DIRECTED BY THE ENGINEER.

ALL WORK REQUIRED TO SET UP, MAINTAIN, AND REMOVE TRAFFIC CONTROL AS DETAILED IN THESE PLANS SHALL BE INCLUDED IN THE COST OF THE ASSOCIATED TRAFFIC CONTROL PAY ITEMS.

**STAGE 3 CONSTRUCTION**

1. MOVE TRAFFIC TO FINAL PROPOSED ALIGNMENT.
2. REMOVE NW PAVEMENT AND TEMPORARY WIDENING
3. EARTHWORK ALONG NW SIDE OF IL 16.
4. BUILD UP REMAINDER OF VARIABLE DEPTH BINDER COURSE.
5. MILL EXISTING PAVEMENT AT THE WEST END OF IL 16, AND ALONG IL 159 AS NECESSARY.
6. PLACE 1" LEVELING BINDER AND 2" SURFACE THROUGHOUT THE LIMITS OF PART A.
7. PLACE BITUMINOUS SHOULDERS AND AGGREGATE SHOULDERS THROUGHOUT THE LIMITS OF PART A.
8. INSTALL PERMANENT SIGNS AS SHOWN IN THE SIGNING DETAIL SHEETS.
9. PLACE TREES AND SEEDING AS SHOWN IN THE LAND-SCAPING PLAN.

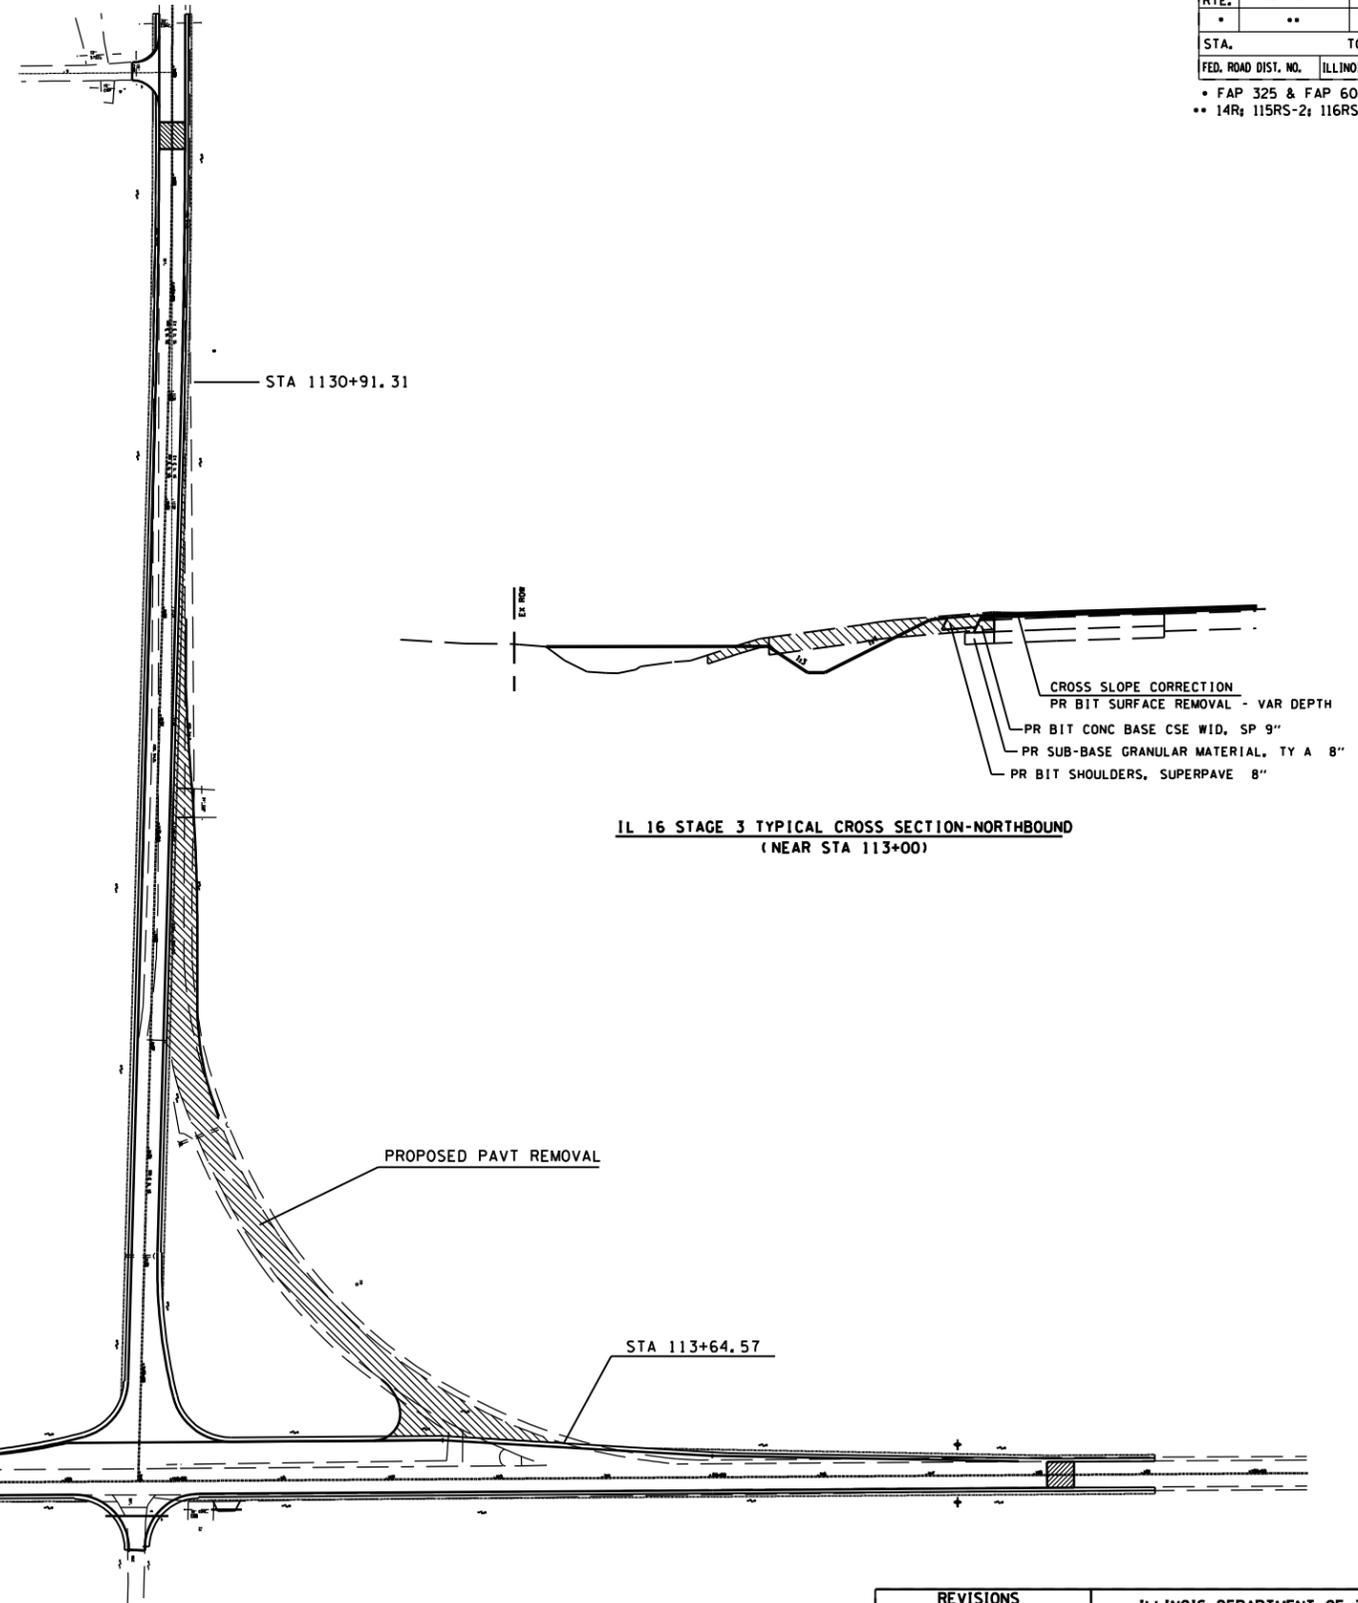

**IL 16 STAGE 3 TYPICAL CROSS SECTION-NORTHBOUND (NEAR STA 113+00)**

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION  
**STAGE 3 CONSTRUCTION**  
 FAP 325 (IL 16) & FAP 604 (IL 159)  
 SECTION 14R; 115RS-2; 116RS-4; 101RS-2  
 MACOUPIN COUNTY  
 SCALE: VERT. \_\_\_\_\_  
 DATE \_\_\_\_\_ HORIZ. \_\_\_\_\_  
 DRAWN BY \_\_\_\_\_  
 CHECKED BY \_\_\_\_\_

PLOT DATE : #DATES  
 FILE NAME : #FILEL#  
 PLOT SCALE : #SCALE#  
 USER NAME : #USER#
